Exhibit C

Rome Tennis Center at Berry College - Indoor Tennis Facility - Project Schedule
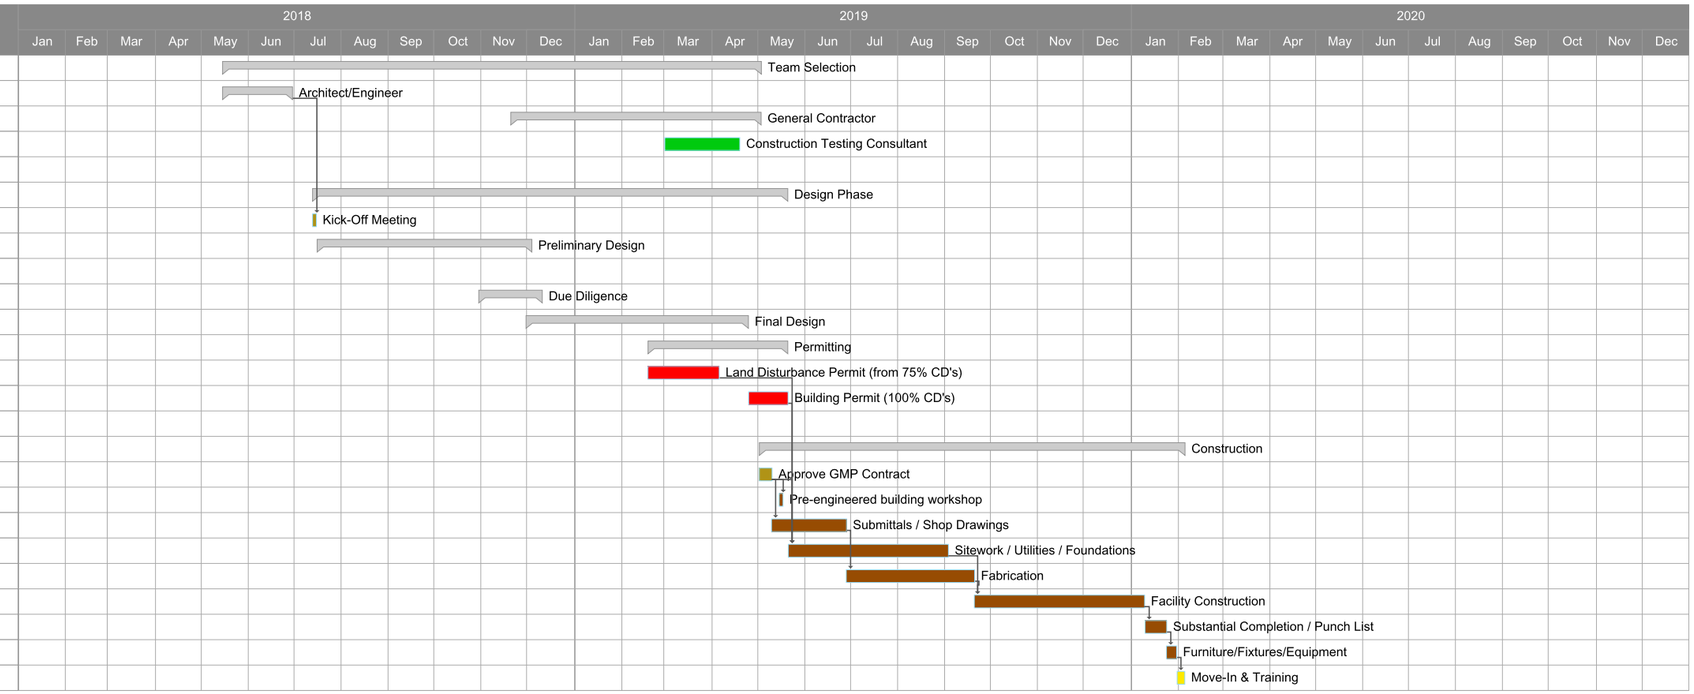
	Task Name	Start	Finish	Predecessors
1	**Team Selection**	**05/15/18**	05/02/19	
2	Architect/Engineer	05/15/18	06/29/18	
6	General Contractor	11/20/18	05/02/19	
12	Construction Testing Consultant	03/01/19	04/18/19	
13				
14	**Design Phase**	07/13/18	05/20/19	
15	Kick-Off Meeting	07/13/18	07/13/18	2FS +9d
16	Preliminary Design	07/16/18	12/03/18	
25				
26	Due Diligence	10/30/18	12/10/18	
30	Final Design	11/30/18	04/24/19	
37	**Permitting**	02/18/19	05/20/19	
38	Land Disturbance Permit (from 75% CD's)	02/18/19	04/05/19	31
39	Building Permit (100% CD's)	04/25/19	05/20/19	36
40				
41	**Construction**	05/02/19	02/04/20	
42	Approve GMP Contract	05/02/19	05/09/19	36FS +5d
43	Pre-engineered building workshop	05/15/19	05/15/19	42FS +3d
44	Submittals / Shop Drawings	05/10/19	06/27/19	42
45	Sitework / Utilities / Foundations	05/21/19	09/02/19	38, 39, 42
46	Fabrication	06/28/19	09/19/19	44
47	Facility Construction	09/20/19	01/09/20	45, 46
48	Substantial Completion / Punch List	01/10/20	01/23/20	47
49	Furniture/Fixtures/Equipment	01/24/20	01/30/20	48
50	Move-In & Training	01/31/20	02/04/20	49
