Tennis Center of Georgia at Berry College
Master Construction Schedule

ID	Task Name	Duration
1	**TENNIS CENTER**	**282 days**
2	**MILESTONES**	**229 days**
3	**CONSTRUCTION START**	**0 days**
4	**SUBSTANTIAL COMPLETON**	**0 days**
5	**OWNER MOVE IN**	**20 days**
6	**FINAL COMPLETON**	**0 days**
7	**PRECONSTRUCTION & DESIGN**	**50 days**
8	**GMP**	**28 days**
9	GMP Drawings Issued	0 days
10	GMP Pricing	16 days
11	GMP Pricing - Review and Reconcilation	5 days
12	GMP Executed / NTP	0 days
13	City Commission Mtg / Approval	0 days
14	Ground Breaking Ceremony	0 days
15	**PERMITS**	**47 days**
20	**PROCUREMENT**	**65 days**
29	**CONSTRUCTION**	**209 days**

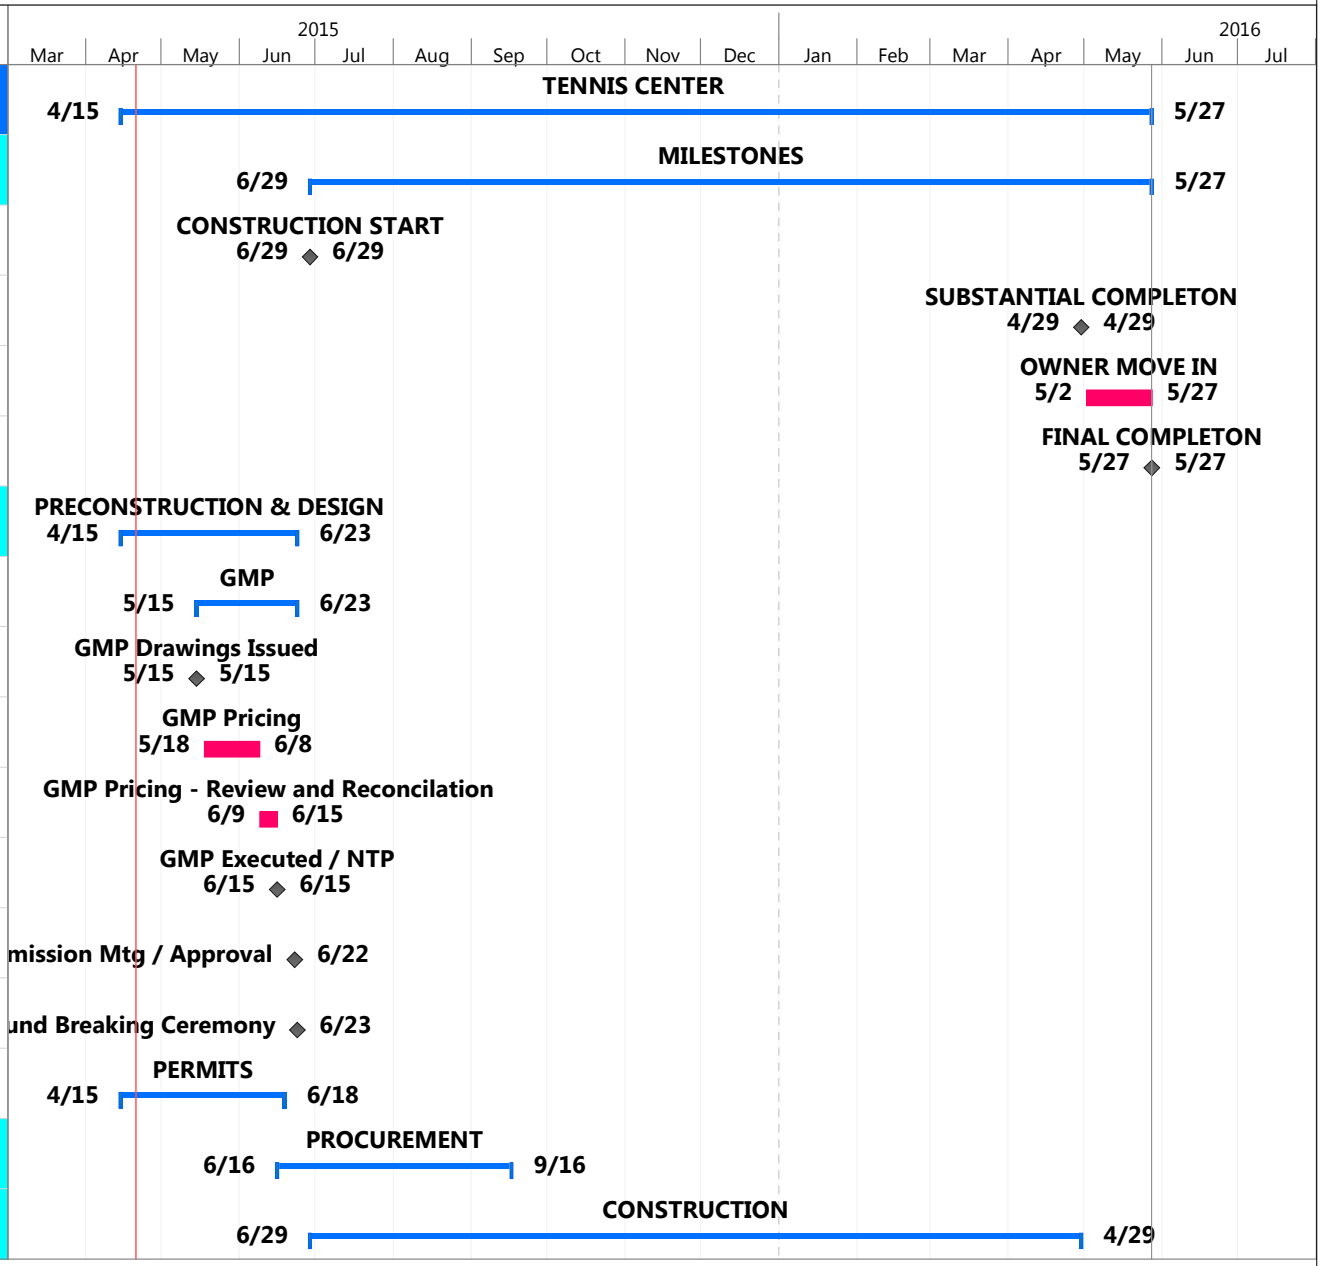

Tennis Center of Georgia at Berry College
Master Construction Schedule

ID	Task Name	Duration
30	Mobilization / Job Site Setup	5 days
31	**SITEWORK & UTILITIES**	**205 days**
32	Preconstruction Meeting with Inspector	0 days
33	Erosion Control	10 days
34	Clearing & Grubbing	10 days
35	Rough Grading	35 days
36	Storm & Sanitary System	30 days
37	Water & Fire Line	20 days
38	Georgia Power Transformers	20 days
39	**TENNIS COURTS**	**147 days**
40	**Phase 1 (approx 20 cts)**	**89 days**
54	**Phase 2 (approx 19 cts)**	**89 days**
68	**Phase 3 (approx 12 cts)**	**82 days**
82	Court Coatings - Color	20 days
83	Court Accessories	15 days
84	**PARKING, LANDSCAPE, & HARDSCAPE**	**135 days**
85	**Parking Lot & Main Drive**	**65 days**

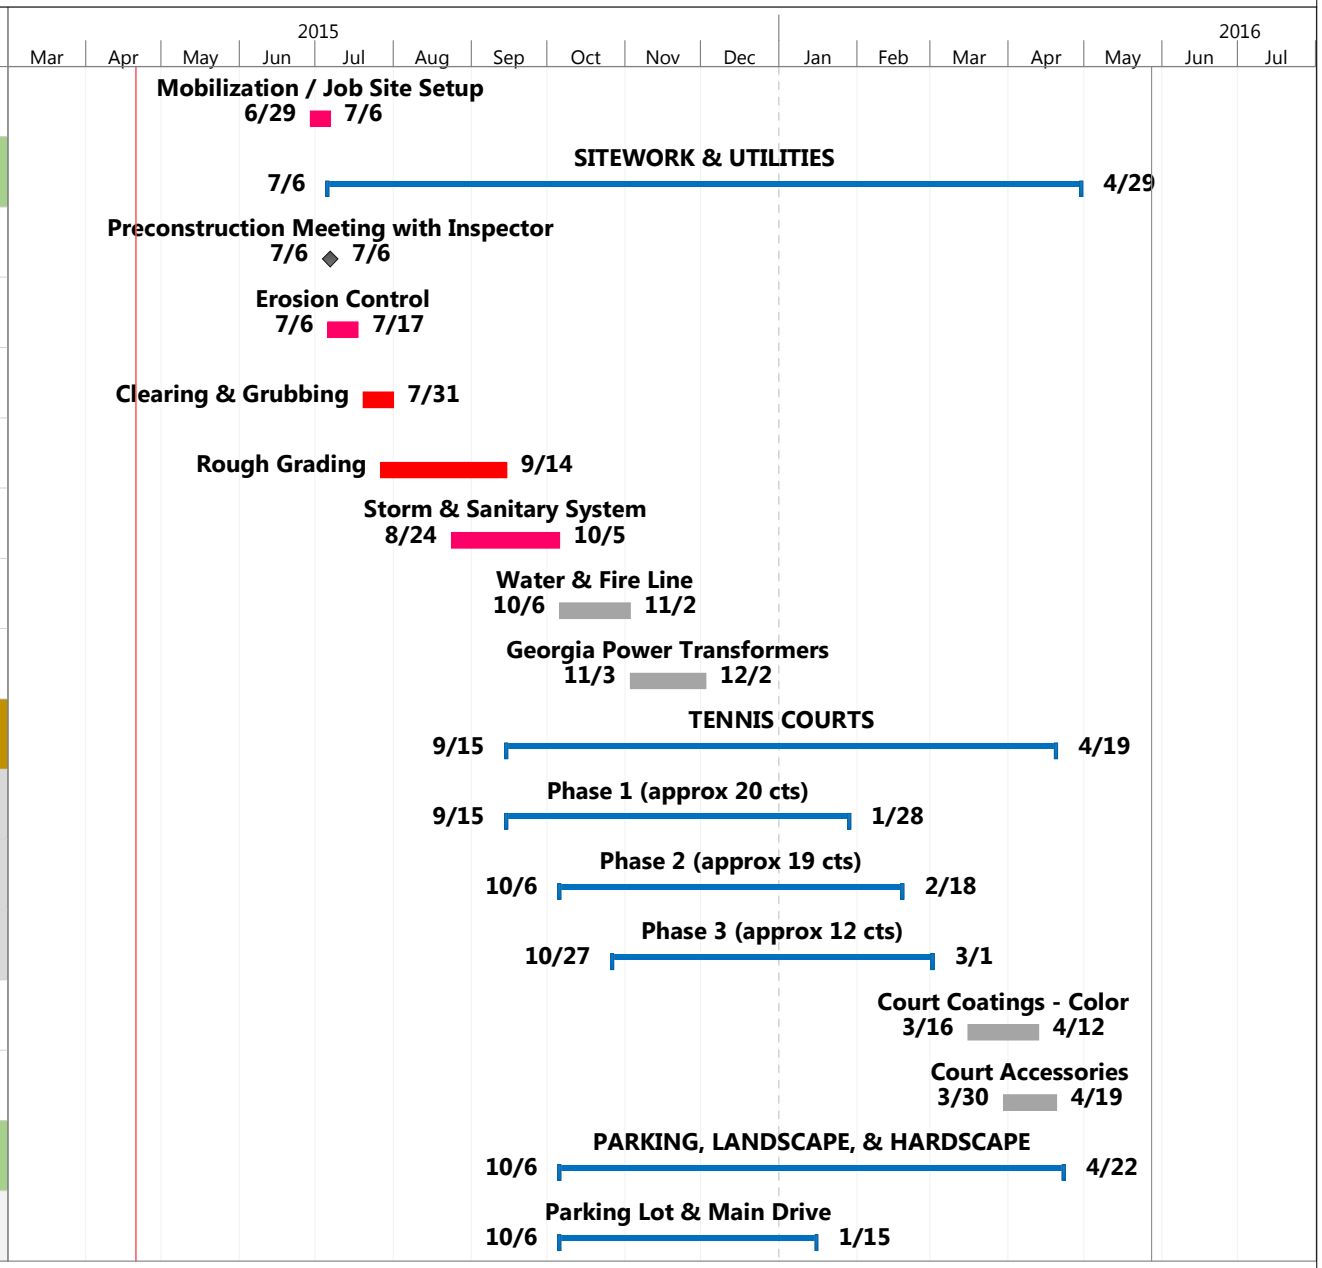

Tennis Center of Georgia at Berry College
Master Construction Schedule
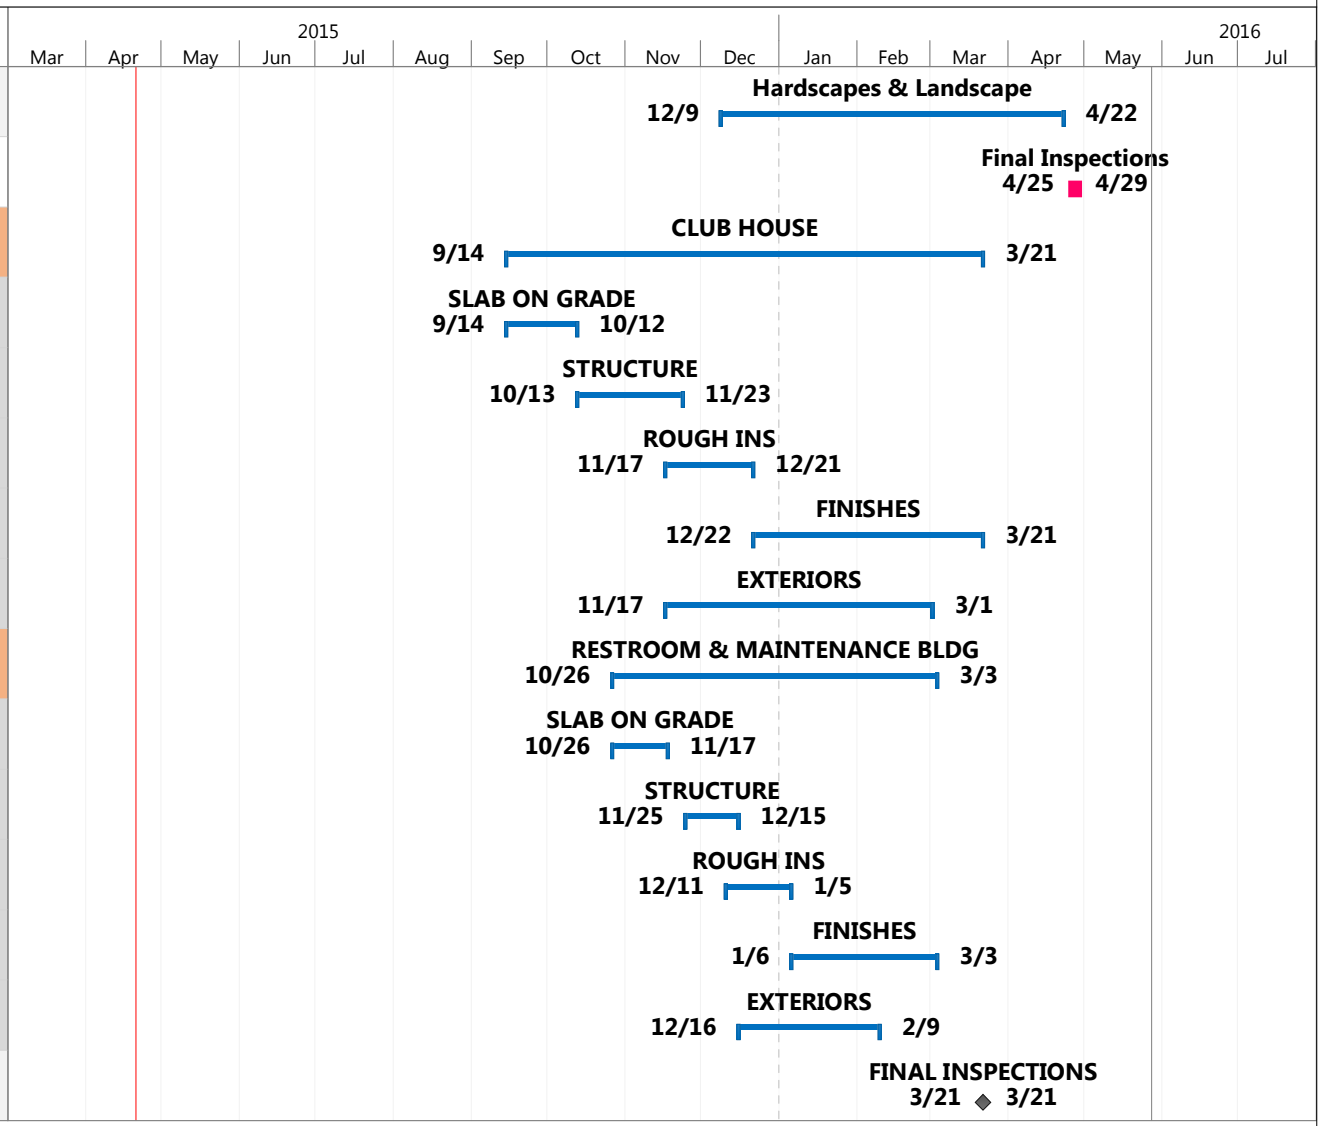
ID	Task Name	Duration
90	**Hardscapes & Landscape**	**91 days**
99	Final Inspections	5 days
100	**CLUB HOUSE**	**126 days**
101	**SLAB ON GRADE**	**20 days**
108	**STRUCTURE**	**30 days**
114	**ROUGH INS**	**23 days**
124	**FINISHES**	**58 days**
142	**EXTERIORS**	**67 days**
150	**RESTROOM & MAINTENANCE BLDG**	**84 days**
151	**SLAB ON GRADE**	**16 days**
158	**STRUCTURE**	**13 days**
163	**ROUGH INS**	**11 days**
168	**FINISHES**	**42 days**
185	**EXTERIORS**	**33 days**
192	**FINAL INSPECTIONS**	**0 days**
